


May 2021, Issue #15

English Version



Valard Construction, was selected by Wataynikaneyap Power to provide engineering, procurement and construction (EPC) solutions for the Wataynikaneyap Power Transmission Project in Northwestern Ontario, Canada.

The scope of work on the project consists of EPC services for more than 1,600 kilometers of transmission and distribution infrastructure ranging in voltage from 25 kV to 230 kV and 22 substations. Valard created this newsletter to provide regular updates on construction activities for the 24 First Nation communities.

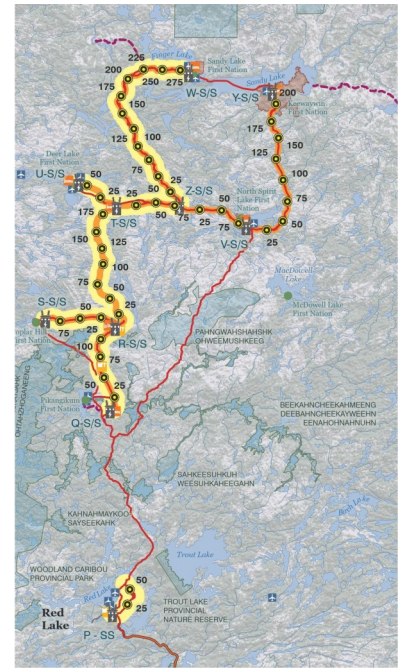


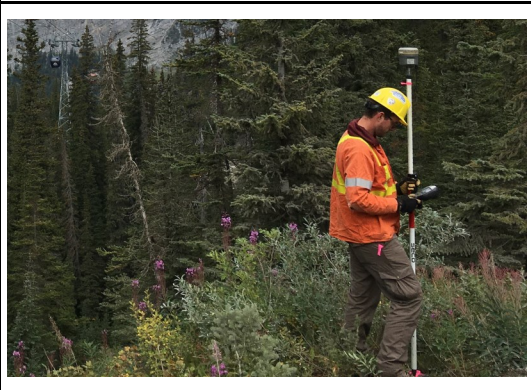
Three-Month Lookahead – Field Activities

Proposed schedule as of May 15, 2021

Period: May 1, 2021 to July 31, 2021


Note: Subject to change based on field conditions.

Group 3 – Transmission Lines

Activity		Detail
	<p>Camp Mobilization and/or Installation</p>	<ul style="list-style-type: none"> Junction Camp (near Berens River) camp operational as of January 2021 Sandy Lake and Poplar Hills camps mobilized
	<p>Survey</p>	<ul style="list-style-type: none"> Set survey control points (Starting activity of all survey operations) Measure existing powerline heights Locate existing underground utilities Work area <ul style="list-style-type: none"> * Red Lake * Deer Lake First Nation to North Spirit Lake First Nation and north to Sandy Lake First Nation

Monthly Project Newsletter




Provided by Valard



May 2021, Issue #15


English Version

Group 3 – Transmission Lines

Activity		Detail
	<p>Clearing and Access</p>	<ul style="list-style-type: none"> • Clearing and Access development <ul style="list-style-type: none"> * Falling, raking, and piling of trees
	<p>Construction</p>	<ul style="list-style-type: none"> • Tower foundation and anchor installation <ul style="list-style-type: none"> * Excavating * Rock drilling • Assembly of steel towers in assembly yards and on ROW • Work area <ul style="list-style-type: none"> * Knox Lake
	<p>Environment</p>	<ul style="list-style-type: none"> • In advance of and during construction activities watercourses and environmentally sensitive areas are flagged and monitored; focusing on erosion, sediment control and spill responses • Archaeology Program conducted by Woodland Heritage accessing approved access plan • Environmental Incident reporting and associated cleanup • Work area <ul style="list-style-type: none"> * Red Lake * Deer Lake First Nation to North Spirit Lake First Nation and north to Sandy Lake First Nation

Monthly Project Newsletter



Provided by Valard



May 2021, Issue #15

English Version


Group 3 – Substations

Activity		Detail
	Substation Survey/ Clearing	<ul style="list-style-type: none">• Setting control points to start surveying• Flagging and inserting stakes in the ground to outline work area• Clearing of substation area and access road development• Substations Work Area:<ul style="list-style-type: none">* Poplar Hill, Deer Lake, Sandy Lake and North Spirit Lake
	Substation Construction	<ul style="list-style-type: none">• Civil and foundation construction• Substations Work Area:<ul style="list-style-type: none">* Red Lake, Poplar Hill, Deer Lake, Sandy Lake and North Spirit Lake

For more activity details visit the website at www.valard-watay.com, or if you have any general inquiries about this newsletter, please contact Wataynikaneyap Power at WatayInquiries@wataypower.ca.

Monthly Project Newsletter

Provided by Valard



May 2021, Issue #15

English Version

Valard is engaging with Participating First Nations to:

- * Learn more about community expectations and interests; as well as identify training, employment, procurement and business opportunities.
- * Engage with Indigenous Relations and Group Project Management to work with Community and Working groups to identify camp locations and services available to support work camps.
- * Facilitate and coordinate Indigenous participations in community businesses, equipment, services, work force, and existing or potential joint ventures.
- * Working with the Communities for open lines of communication for COVID-19 updates with regards to travel and quarantine directives.
- * Provide notification of encounters with sensitive wildlife such as Caribou sightings to communities near the encounter.
- * Provide the Chief and Council of any additional temporary work packages with Territorial area maps included: Permit to Take Water, Helicopter Pads and any additional camp locations if required.
- * Utilizing the Construction Liaisons to help coordinate ongoing communication between Project Management and Community Leadership and other duties such as: setting up job fairs, social media upkeep, coordinating employment and business opportunities and acting as a direct link to the Chief and/or Council of various communities.

Indigenous Relations Advisor for Group 3

- ◇ Sandy Lake First Nation—Bart Meekis

Valard Group 3 Construction Liaisons:

- ◇ Pikangikum First Nation—Tracy Black
- ◇ North Spirit Lake First Nation—Donald Campbell
- ◇ McDowell Lake First Nation—Charles Lawson
- ◇ Sandy Lake First Nation—Robert Keith Linklater
- ◇ Keewaywin First Nation—Kieran Sakakeep
- ◇ Poplar Hill First Nation—Georgina Suggashie
- ◇ Deer Lake First Nation—Vacant

Valard Indigenous Relations Team Introduction:

The Valard Indigenous Relations Team consists of the following members for the Wataynikaneyap Power Transmission Project and can be contacted at Watay-IndigenousRelations@valard.com:

- * **Blaine Collett**—Sr. Director Indigenous Relations
- * **Alex McGillivray**—Sr. Manager, Stakeholder Engagement
- * **Terrance Bob**—Indigenous and Stakeholders Relations Liaison
- * **Randal Courchene**—Indigenous and Stakeholders Relations Liaison
- * **Sherice Paizen**—Indigenous Relations Project Assistant

Monthly Project Newsletter

Provided by Valard



May 2021, Issue #15

English Version

Health and Safety

- * **Valard is following the most up to date medical advice provided by federal and provincial government in its own measures to help limit the spread of Covid-19.**
- * Ongoing Covid-19 screening program, camp inspections, program audits and response drills
- * Hazard analysis and control planning every day
- * Development, implementation and monitoring of safe work procedures including preparation for upcoming helicopter work activities
- * Project onboarding, orientation and training/development of workers
- * Emergency preparedness and planning, mock emergency drills completed
- * Joint Health and Safety Committee Involvement
- * Promotion of project's Alcohol & Drug policy, Maintenance Support Security Program and Employee Assistance Program
- * Security Protocols implementation and monitoring
- * Fall Protection and Rescue Planning for tower climbing Best Practices
- * Subcontractor safety support, onboarding, compliance observations, and audits
- * Valard COVID-19 Vaccination program for eligible employees



Employment Opportunities

- * Valard Construction invites members of the Participating First Nations to apply for the following positions:

Administrative Assistant

Assemblers

Class A Driver

Community Support Partner

Drafting Technician

Emergency Medical Responder

Environmental Monitor

Excavator Operator

Foundations Labourer

Fuel Truck Driver

General Foreperson/Construction Supervisor

Heavy Duty Technician

Journeyman Automotive Service Technician

Prep/Ground Work Subforeperson

Primary Care Paramedic

Project Assistant

Project Field QC

Project Safety Admin

Please forward resumes to: watay-resumes@valard.com and projectjobs@oslp.ca

For more updates please visit the Valard project website (www.valard-watay.com) or:

Call: 807-345-2395

<https://www.facebook.com/watayproject>

<https://www.facebook.com/OpiikapawiinServicesLP>

<https://www.facebook.com/Wataynikaneyap-Power>

<https://www.oslp.ca>—Please visit OSLPs site for a full list of available positions

**If you have any general inquiries about this newsletter, please contact
Wataynikaneyap Power at WatayInquiries@wataypower.ca.**
